

Lab 02 - Agile Backlog Creation & Sprint Simulation in Jira

Name: Vishruta

Class: I

SRN: PES1UG24CS5338


Spaces / Remote Team Time-Tracking & Project Approver

RTTTPA board

Summary Timeline Active sprints Backlog Calendar List Forms Development Docs Reports +

Ask AI Search work Filter Group

☐	Work	Assignee	Reporter	Priority	Status	Resolution	Created	Updated	Due date	
☐	> RTTTPA-1 Epic 1: Time Logging & Ticket Validation	Unassigned	V Vishruta	High	Done	Unresolved	02 Sept 2026, 18:50	20 Sept 2026, 21:33	9 Sept 2026	...
☐	> RTTTPA-2 Epic 2: Timesheet Submission & Manager Approval	Unassigned	V Vishruta	High	Done	Unresolved	02 Sept 2026, 18:52	20 Sept 2026, 21:33	9 Sept 2026	...
☐	> RTTTPA-3 Epic 3: Project Budget Burn Visibility	Unassigned	V Vishruta	High	Done	Unresolved	02 Sept 2026, 18:55	20 Sept 2026, 21:33	9 Sept 2026	...
☐	> RTTTPA-11 Epic 4: Resource Allocation and Capacity Planning	Unassigned	V Vishruta	High	Done	Unresolved	02 Sept 2026, 21:05	20 Sept 2026, 21:33	16 Sept 2026	...
☐	> RTTTPA-12 Epic 5: Reporting and Dashboard Enhancements	Unassigned	V Vishruta	High	Done	Unresolved	02 Sept 2026, 23:20	20 Sept 2026, 21:33	16 Sept 2026	...

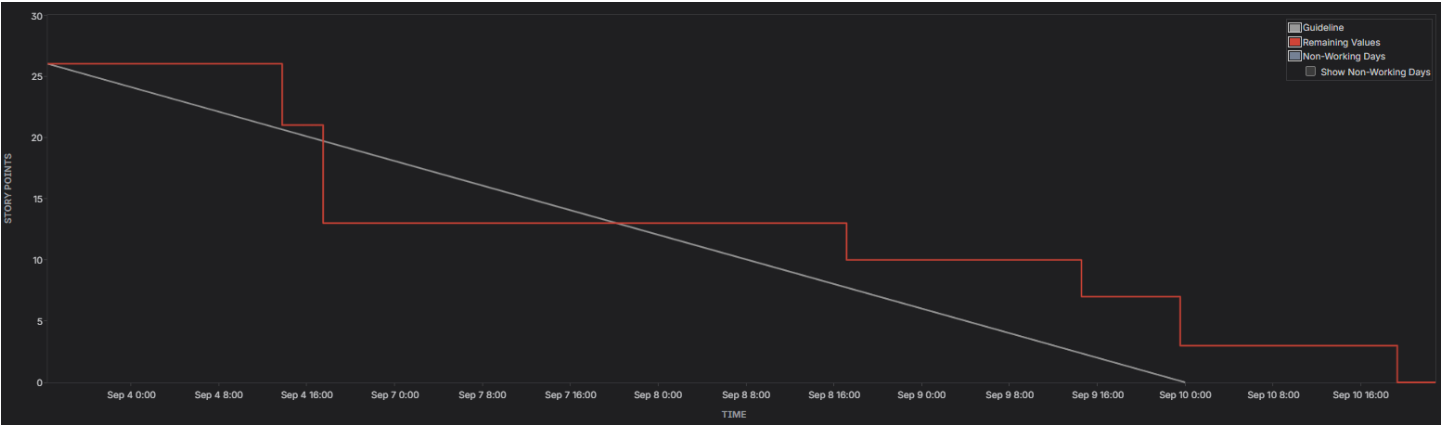

Track the remaining work for Sprint 2 (6 stories)



Status Report

TIME

Completed Issues

[View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (26)
RTTTPA-4	1.1 — Log Time Against a Ticket	 Story	 High	DONE	5
RTTTPA-5	1.2 — Validate Ticket ID When Logging Time	 Story	 High	DONE	3
RTTTPA-6	2.1 — Submit Weekly Timesheet for Approval	 Story	 High	DONE	5
RTTTPA-7	2.2 — Approve a Submitted Timesheet	 Story	 High	DONE	3
RTTTPA-8	2.3 — Reject a Timesheet with a Reason	 Story	 Medium	DONE	3
RTTTPA-9	3.2 - Recalculate Budget Burn on Timesheet Approval	 Story	 Medium	DONE	4
RTTTPA-10	3.1 — View Real-Time Project Budget Burn Rate	 Story	 Medium	DONE	3

Status Report

Completed Issues

[View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (23)
RTTTPA-13	Enforce 24-hour daily time-entry limit for developers	 Story	 High	DONE	5
RTTTPA-14	Submit timesheet for manager approval	 Story	 High	DONE	3
RTTTPA-15	Review and approve or reject timesheets	 Story	 High	DONE	5
RTTTPA-16	Display project budget burn charts on dashboards	 Story	 High	DONE	4
RTTTPA-17	Update approval status on dashboards within 500 ms	 Story	 Medium	DONE	3
RTTTPA-18	Ensure secure dashboard updates under peak load	 Story	 Medium	DONE	3

Reflection Answers

1. Did your estimations reflect the actual effort?

The story point estimations generally reflected the actual effort required to complete the work. The Fibonacci-based points Generally did help represent the relative complexity and uncertainty of the user stories. As the stories were completed during the simulated sprints, the burndown charts showed a gradual reduction in the remaining story points. This indicates that the estimates were somewhat reasonably aligned with the effort involved.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized according to the importance and user impact of the requirements. High-priority stories related to core time tracking, timesheet submission and approval, and project budget visibility were addressed first. This helped ensure that the most important functionality was included in the sprints before lower-priority work.

3. How did your simulated sprint align with your plan?

The simulated sprints generally followed the planned workflow but rather haphazardly. The selected user stories were moved from To Do to In Progress and then to Done as the work was completed. The burndown charts showed the reduction of remaining story points throughout the sprint, indicating that the planned work was progressively completed. Some work was completed at different times during the sprint, which resulted in uneven drops in the burndown chart.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts provided a clear view of how much work remains throughout each sprint and how quickly the team was completing the planned work. The comparison between the remaining values line and the guideline helped identify whether progress was occurring as planned. The uneven drops also showed that work was not completed at a constant rate, which is expected when stories have different sizes and completion times. Overall, the charts provided a useful indication of the team's progress and capacity during the simulated sprints.
